



PT. ANDEKJA PUTRA

GENERAL CONTRACTOR & SUPPLIER

Jl. Bonerate No. 6 Tlp : (0411) 3631527 - 3617158 Makassar

Nomor : 13-13/KMU-PT/BRBL/MKS/I/2026
Lampiran : 1 (set)
Perihal : Permohonan Perpanjangan
Jangka Waktu Pekerjaan

Kepada Yth,
Manager
PT. PLN (Persero) UPT Makassar
Di –
Tempat

Dengan Hormat,

Sehubungan dengan Proyek "Pengadaan dan Pemasangan Kubikel 20 kV GI Barru dan GI Balusu" Kontrak No : 005.PJ/DAN.01.03/F47010000/2024, Tanggal 10 Juni 2025. Bersama surat ini, kami sampaikan perkembangan pelaksanaan pekerjaan hingga saat ini, sebagai berikut :

1. Progress pekerjaan hingga saat ini telah mencapai 27,381%.
2. Pada tanggal 21 Juni 2025, surat permohonan data eksisting telah kami sampaikan.
3. Pada tanggal 24 Juni 2025, surat penyampaian hasil survei kubikel di GI Barru dan GI Balusu telah kami sampaikan.
4. Pada tanggal 25 Agustus 2025, surat permohonan persetujuan teknis telah kami sampaikan.
5. Pada tanggal 16 September 2025, dokumen persetujuan teknis kami telah dikembalikan untuk dilakukan penyesuaian dan pengajuan ulang ke pihak manufaktur.
6. Menindaklanjuti hal tersebut, pada tanggal 17 September 2025 kami kembali mengajukan permohonan persetujuan teknis material kubikel.
7. Pada tanggal 20 September 2025, kami juga telah menyampaikan surat permohonan pelaksanaan Design Review Meeting (DRM) bersama pihak ABB.
8. Terkait hal tersebut, pembahasan persetujuan teknis (DRM) telah dilaksanakan pada tanggal 24–25 September 2025 (MoM terlampir).
9. Berdasarkan hasil pembahasan tersebut, terdapat beberapa perubahan pada gambar persetujuan teknis yang memerlukan proses penyesuaian ulang bersama pihak manufaktur.
10. Pada tanggal 06 Oktober, persetujuan teknis hasil penyesuaian sesuai dengan hasil DRM telah kami ajukan kembali.
11. Terkait pengajuan tersebut, pada tanggal 27 November 2025 dokumen persetujuan teknis kami telah dikembalikan untuk direview dan memulai proses pabrikasi.
12. Pada tanggal 07 Oktober 2025, melalui surat kami No. 09-07/KMU-PT/BRBL/MKS/X/2025 , perihal "Permohonan Data Eksisting" Tanggal 07 Oktober, kami kembali menyampaikan permohonan Data Eksisting kepada pihak end user.
13. Terkait point 12, menindaklanjuti hal tersebut pada tanggal 20 Oktober 2025 Eksisting telah kami terima. Namun, Schematic Drawing CRP eksisting GI Barru belum kami terima.
14. Berdasarkan beberapa hal di atas, serta adanya perubahan pada TPG dan Schematic Drawing untuk material Kubikel GI Barru dan GI Balusu, maka pihak manufaktur memerlukan waktu tambahan dalam proses penyesuaian dan produksi.



PT. ANDEKJA PUTRA

GENERAL CONTRACTOR & SUPPLIER

Jl. Bonerate No. 6 Tlp. : (0411) 3631527 - 3617158 Makassar

Sehubungan dengan hal tersebut, kami memohon perpanjangan waktu pelaksanaan pekerjaan selama 115 (Seratus Lima Belas) hari kalender agar seluruh proses dapat dilaksanakan dengan optimal dan sesuai spesifikasi teknis yang telah disepakati.

Demikian kami sampaikan. Atas perhatian dan kerja sama yang baik, kami ucapkan terima kasih.

Hormat Kami,

Makassar, 13 Januari 2026

PT. Andekja Putra

Fikaori Wira Nasution

Project Manager

Nama Proyek : Pengadaan dan Pemasangan Peralatan Kubikel 20 KV GI Baru dan GI Belusu
No. Kontrak : 005.PJ/DAN.01.03/F47010000/2025
Tanggal Kontrak : 10 Juni 2025
Pelaksana : PT. Andekja Putra

JADWAL PELAKSANAAN PEKERJAAN


Bulan : Oktober 2025
Periode : 05
Pelaksanaan : 240 Hari



Approval Drawing
PO Material
Manufacture Pabrikasi
Pengiriman & Material On Site
Jasa

Makassar, 14 Januari 2026
Dibuat Oleh
PT. Andekja Putra
Fikroli W Nasution
Project Manager

6. Project Schedule - GI Barru & GI Balusu - Andekja Project_13 Jan'26.mpp

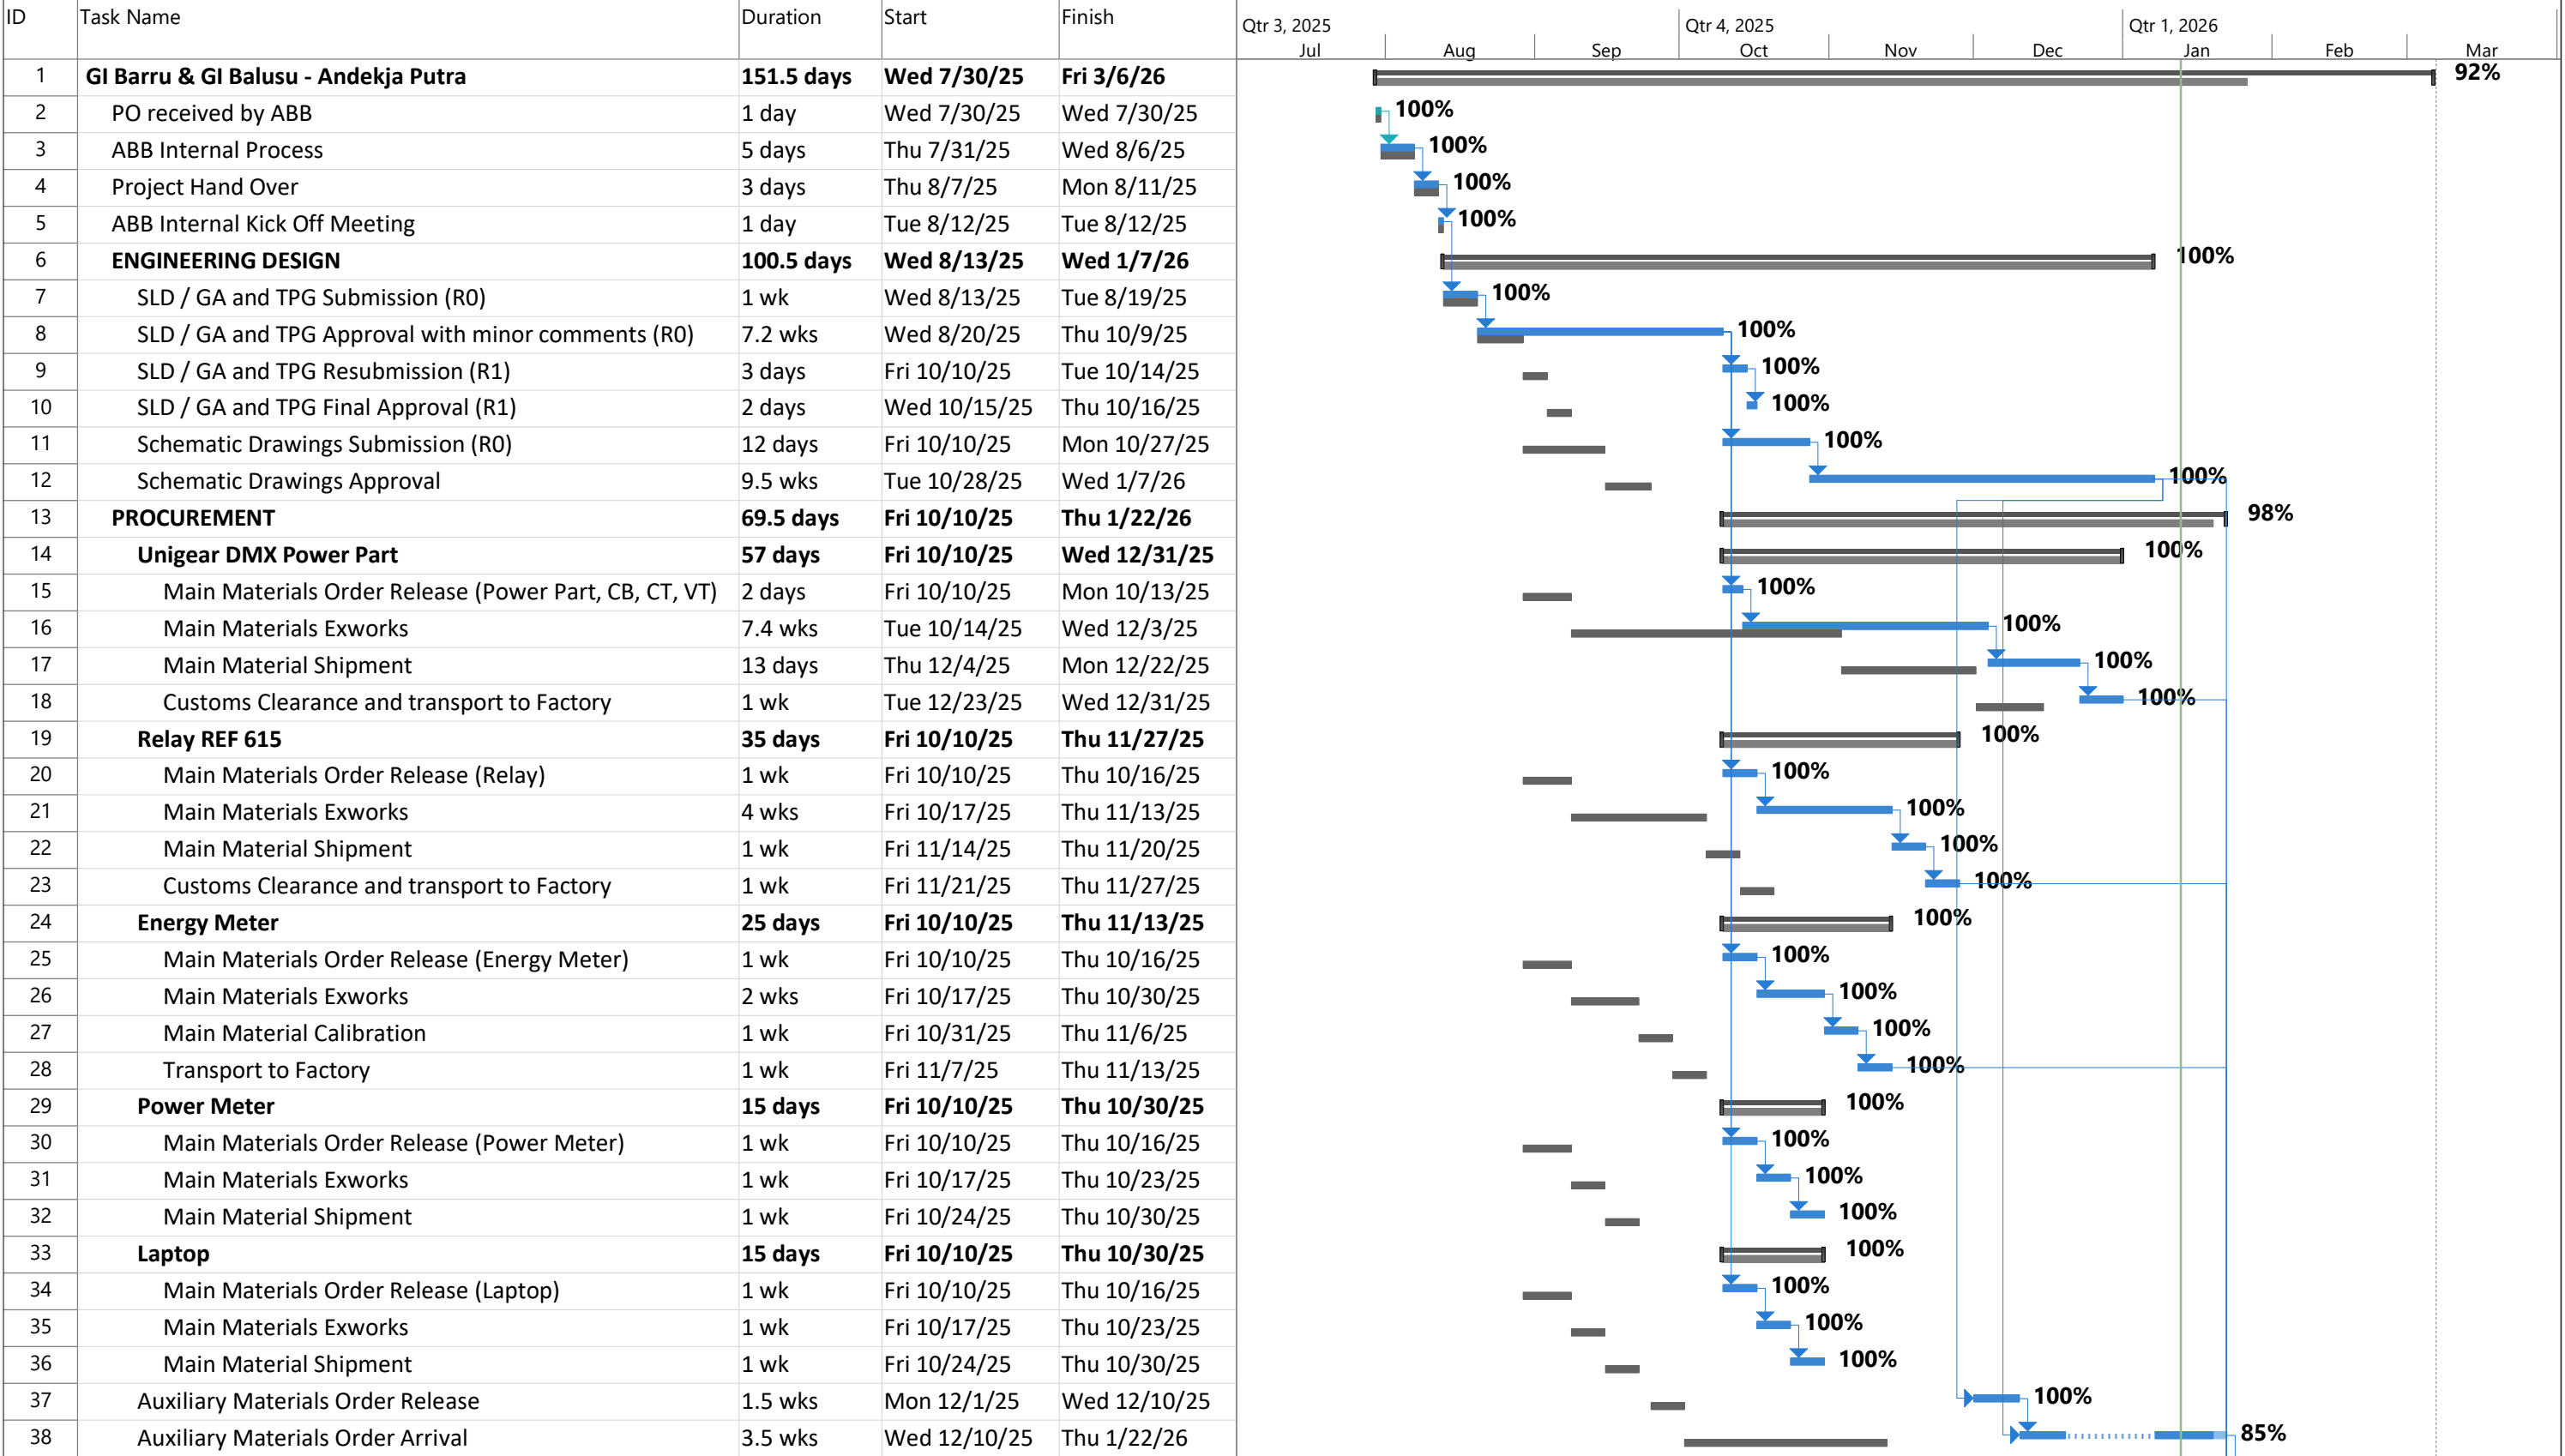

Critical	<div></div>	Split	<div></div>	Finish-only	<div></div>	Baseline Milestone	<div></div>	Manual Summary	<div></div>	Inactive Task	<div></div>
Critical Split	<div></div>	Task Progress	<div></div>	Duration-only	<div></div>	Milestone	<div></div>	Project Summary	<div></div>	Inactive Milestone	<div></div>
Critical Progress	<div></div>	Manual Task	<div></div>	Baseline	<div></div>	Summary Progress	<div></div>	External Tasks	<div></div>	Inactive Summary	<div></div>
Task	<div></div>	Start-only	<div></div>	Baseline Split	<div></div>	Summary	<div></div>	External Milestone	<div></div>	Deadline	<div></div>

6. Project Schedule - GI Barru & GI Balusu - Andekja Project_13 Jan'26.mpp

ID	Task Name	Duration	Start	Finish	Qtr 3, 2025 Jul	Aug	Sep	Qtr 4, 2025 Oct	Nov	Dec	Qtr 1, 2026 Jan	Feb	Mar
39	MANUFACTURING	27 days	Thu 1/22/26	Mon 3/2/26									21%
40	Production Works	2 wks	Thu 1/22/26	Thu 2/5/26									50%
41	Internal Testing	2 wks	Fri 2/6/26	Fri 2/20/26									0%
42	FAT with Customer	1 day	Tue 2/24/26	Wed 2/25/26									0%
43	Punchlist Closing	3 days	Wed 2/25/26	Mon 3/2/26									0%
44	DELIVERY	4 days	Mon 3/2/26	Fri 3/6/26									0%
45	Packing	3 days	Mon 3/2/26	Thu 3/5/26									0%
46	Ex-works Tangerang Factory	1 day	Thu 3/5/26	Fri 3/6/26									0%

Critical	<div></div>	Split	<div></div>	Finish-only	<div></div>	Baseline Milestone	<div></div>	Manual Summary	<div></div>	Inactive Task	<div></div>
Critical Split	<div></div>	Task Progress	<div></div>	Duration-only	<div></div>	Milestone	<div></div>	Project Summary	<div></div>	Inactive Milestone	<div></div>
Critical Progress	<div></div>	Manual Task	<div></div>	Baseline	<div></div>	Summary Progress	<div></div>	External Tasks	<div></div>	Inactive Summary	<div></div>
Task	<div></div>	Start-only	<div></div>	Baseline Split	<div></div>	Summary	<div></div>	External Milestone	<div></div>	Deadline	<div></div>

Order Confirmation

Dear Customer,

We are pleased to have your order for PT. ABB Sakti Industri ELDS Business (ABB) with PO / Contract No. 01-21/AP-PT/PO20KVBB/MKS/VII/2025 dated 30.07.2025.

Herewith we confirmed your order with our project references as below data

Project Name	: GI Barru & GI Balusu
Project No.	: BG325036 – PT. Andekja Putra
SO No.	: 3100160600

Will be delivered as below schedule (latest by)

Handover date	: 07.08.2025
Down payment invoice date	: 08.08.2025
ABB SLD-GA & TPG Approval submission date	: 19.08.2025
Customer SLD-GA & TPG Approval deadline	: 29.08.2025
Customer SLD-GA & TPG Approval actual	: 09.10.2025
Down payment receipt date deadline	: 19.08.2025
ABB Schematics Approval submission date	: 15.09.2025
Customer Schematics Approval deadline	: 24.09.2025
Customer Schematics Approval actual	: 07.01.2026
FAT date	: 14.01.2026
Adjusted FAT date	: 24.02.2026
Ex-work ABB Tangerang date	: 27.01.2026
Adjusted Ex-work ABB Tangerang date	: 06.03.2026

If the schedule mentioned above cannot be met, the following conditions will apply:

1. Any delay in approval from your side will impact the FAT schedule and Ex-works date.
2. Any changes requested after design freeze will give ABB the right to revise the delivery schedule and apply additional price as a result of such changes.
3. If the down payment (DP) is not paid within three (3) months after invoicing, or the project is on hold for more than three (3) months, or there is no confirmation on the approval drawings for more than three (3) months, resulting in a delivery delay exceeding eight (8) months, ABB reserves the right to adjust the prices unless stated otherwise in an official agreement between both parties (Contract Terms and Conditions).
4. If two (2) weeks after the material ex-works date, the goods cannot be picked up or ABB is not permitted to deliver due to site unavailability or other reasons from your side, the goods will be sent to a third-party warehouse. Storage charges will be applied to you. Any risks during storage will be transferred to you, and the warranty period will commence.
5. Any conditions not listed above shall follow ABB's Standard Terms and Conditions or the agreed Terms and Conditions in the Contract.

This order confirmation forms an integral and inseparable part of the PO/Contract No. as referenced above.



For any matters related to this project, please contact the undersigned.

PT. ABB Sakti Industri

Panji Fakhruzzaman

Project Manager

Email: panji.fakhruzzaman@id.abb.com

Mobile Phone No.: +6282189907050
